


ID	Task Name	Duration	Start	Finish	Predecessor	Resource Names
1	RESURFACING 2020	70 days	Wed 4/15/20	Tue 7/21/20		
2	GROUP E	0 days	Wed 4/15/20	Wed 4/15/20		ELLEN AVE
3	MG&E	5 days	Wed 4/15/20	Tue 4/21/20		OFFSETS DURING STORM INSTALL
4	STORM	8 days	Wed 4/15/20	Fri 4/24/20		WORK WITH MGE ON WINDOWS
5	CURB & GUTTER	16 days	Wed 4/15/20	Wed 5/6/20		
6	PULVERIZE	10 days	Mon 5/11/20	Fri 5/22/20		
7	PAVE	2 days	Mon 5/25/20	Tue 5/26/20		
8						
9	GROUP A	0 days	Mon 4/27/20	Mon 4/27/20		LIEN RD
10	STORM	10 days	Mon 4/27/20	Fri 5/8/20		
11	CURB & GUTTER	3 days	Mon 5/4/20	Wed 5/6/20		
12	MILL	3 days	Mon 5/11/20	Wed 5/13/20		
13	PAVE	2 days	Thu 5/14/20	Fri 5/15/20		
14						
15	GROUP G	0 days	Mon 4/27/20	Mon 4/27/20		INDEPENDENCE LN
16	MG&E	5 days	Mon 4/27/20	Fri 5/1/20		OFFSET DURING STORM INSTALL
17	STORM	10 days	Tue 5/19/20	Mon 6/1/20		WORK WITH MGE ON WINDOWS
18	CURB & GUTTER	5 days	Mon 6/1/20	Fri 6/5/20		
19	PULVERIZE	3 days	Mon 6/8/20	Wed 6/10/20		
20	PAVE	1 day	Thu 6/11/20	Thu 6/11/20		
21						
22	GROUP F	0 days	Mon 4/27/20	Mon 4/27/20		S STOUGHTON RD
23	MG&E	14.5 days	Mon 4/27/20	Fri 5/15/20		REPLACE STEEL GAS MAIN
24	STORM	3 days	Wed 5/6/20	Fri 5/8/20		
25	CURB & GUTTER	4 days	Mon 5/11/20	Thu 5/14/20		
26	PULVERIZE	12 days	Tue 5/19/20	Wed 6/3/20		
27	PAVE	1 day	Thu 6/4/20	Thu 6/4/20		
28						
29	GROUP D	0 days	Mon 5/11/20	Mon 5/11/20		H CROSSING BLVD
30	CURB & GUTTER	12 days	Mon 5/11/20	Tue 5/26/20		
31	MILL	10 days	Mon 6/1/20	Fri 6/12/20		
32	PAVE	2 days	Mon 6/15/20	Tue 6/16/20		
33						
34	GROUP B	0 days	Wed 6/3/20	Wed 6/3/20		S BROOKS ST
35	STORM	8 days	Wed 6/3/20	Fri 6/12/20		
36	CURB & GUTTER	6.5 days	Tue 6/9/20	Wed 6/17/20		
37	MILL	5 days	Mon 6/22/20	Fri 6/26/20		
38	PAVE	1 day	Mon 6/29/20	Mon 6/29/20		
39						
40	GROUP C	0 days	Mon 5/25/20	Mon 5/25/20		HATHAWAY DR
41	MG&E	20 days	Mon 5/25/20	Fri 6/19/20		REPLACE STEEL GAS MAIN & SERVICES
42	STORM	10 days	Mon 6/8/20	Fri 6/19/20		
43	CURB & GUTTER	15 days	Mon 6/15/20	Fri 7/3/20		
44	PULVERIZE	10 days	Mon 7/6/20	Fri 7/17/20		
45	PAVE	2 days	Mon 7/20/20	Tue 7/21/20		

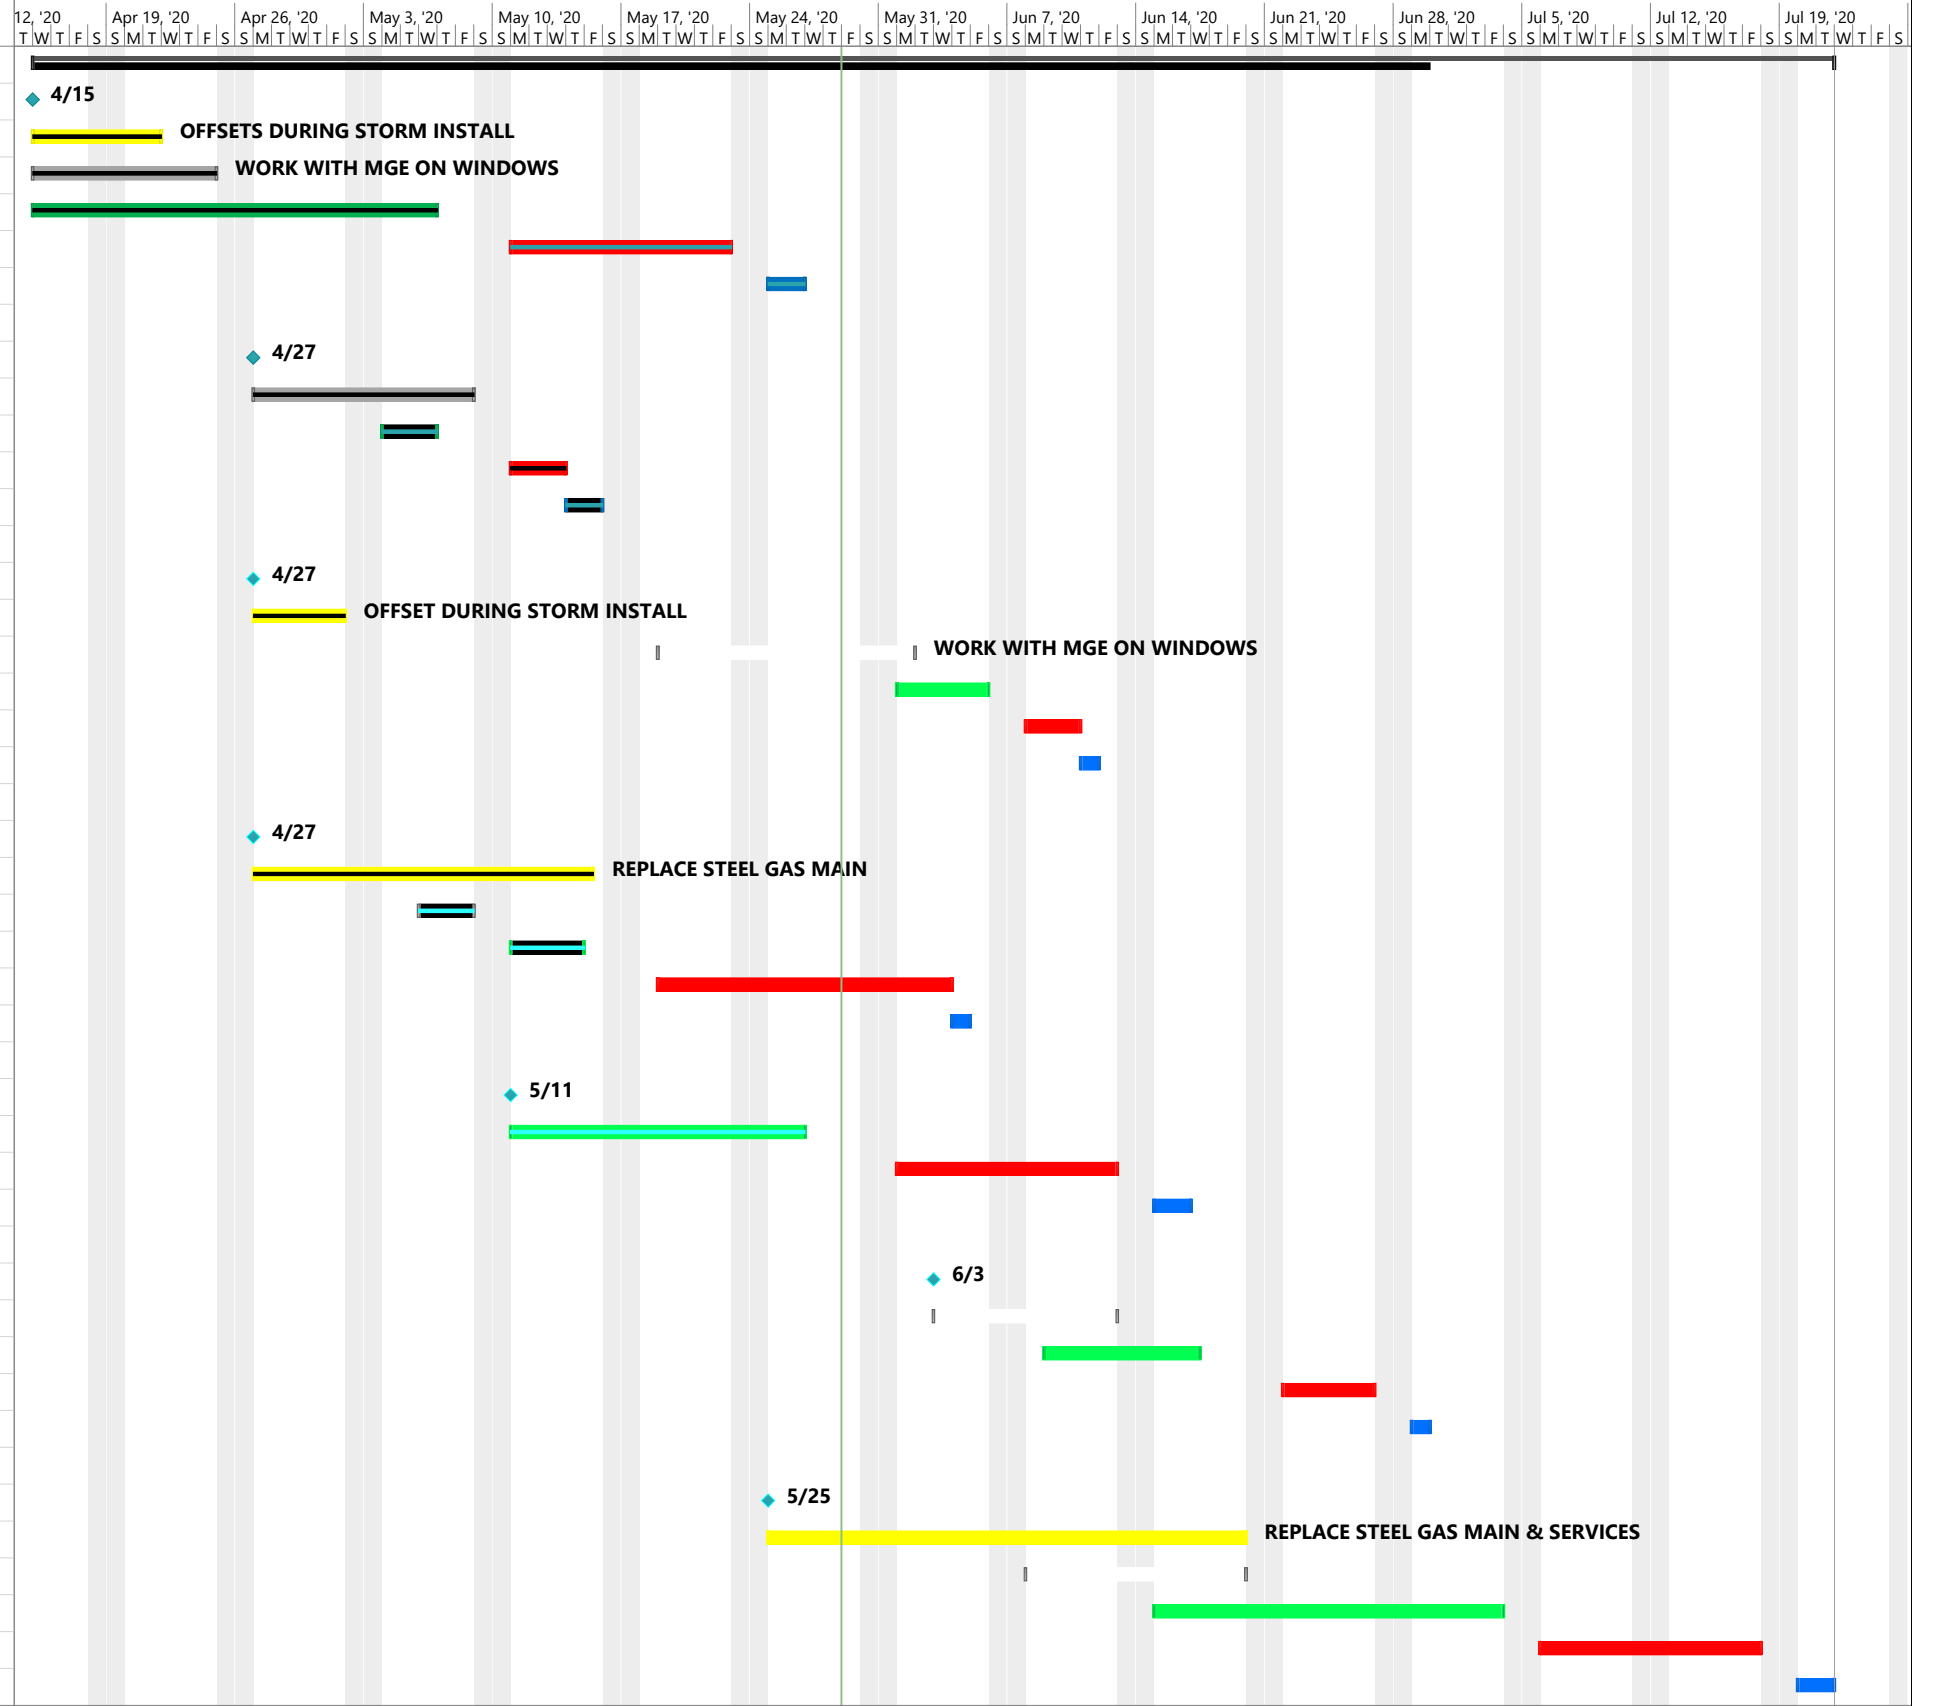

Project: 0221a
Date: Fri 5/29/20

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline		Progress	
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks					
