



Department of Public Works
Engineering Division
James M. Wolfe, P.E., City Engineer

City-County Building, Room 115
210 Martin Luther King, Jr. Boulevard
Madison, Wisconsin 53703
Phone: (608) 266-4751
Fax: (608) 264-9275
engineering@cityofmadison.com
www.cityofmadison.com/engineering

Assistant City Engineer
Bryan Cooper, AIA
Gregory T. Fries, P.E.
Chris Petykowski, P.E.

Deputy Division Manager
Kathleen M. Cryan

Principal Engineer 2
John S. Fahmeyer, P.E.
Janet Schmidt, P.E.

Principal Engineer 1
Mark D. Moder, P.E.
Fadi El Musa Gonzalez, P.E.
Andrew J. Zwieg, P.E.

Financial Manager
Steven B. Danner-Rivers

May 21, 2024

To: Property Owners and Residents along Rutledge Street and Division Street

Re: Street Reconstruction Construction Date Change


City Engineering would like to inform residents on Rutledge Street that the street reconstruction has been moved from 2024 to 2025. When putting together the final design plan for the project, Rutledge Street ended up requiring a significant amount of new storm sewer to be installed to address drainage issues. The addition of the new storm sewer directly conflicts with MG&E's gas mains and services because both utilities are at the same depth underground. MG&E needs to resolve these conflicts first so that construction of Rutledge Street can progress safely and efficiently. Unfortunately, due to the nature of how the designs on these types of project develop, storm sewer is typically the last component to be designed, so these conflicts, and starting the process to find solutions, happened quite late in the design process.

MG&E is currently working on their final plans to modify their gas mains and services to resolve those conflicts. Given the number of anticipated conflicts, we know that this work will be significant and likely take several weeks to complete, but specifics on their final plans are still not known. Construction crew availability will also be a factor as MG&E crews are currently working on other City projects that already underway, along with private developments needing services, and also similar work in other communities that they serve. With the uncertainty on the final plans and very limited crew availability, especially in the immediate future, it won't be possible to complete all of the work on Rutledge Street this year, and we wanted to communicate that as soon as that became clear.

On projects with several different streets and multiple blocks to work on, the City's contractor and MG&E can sometimes coordinate crews and be on the same project at the same time. However, the project on Rutledge Street has comparatively very limited space to work, few access points, and a lot of driveways that will need access for much of the project. It wouldn't be reasonable to try to fit all the necessary materials (pipe, gravel, trench backfill, etc.), equipment, trucking access, and resident access through the Rutledge Street project area if both the City's contractor and MGE's contractor were trying to complete all of their work at the same time.


We anticipate that MG&E's work will likely take place this fall and potentially very early in 2025, with the City's project likely starting once weather allows. We will continue to post updates to the project page as we have more information. If you haven't done so already, you can also subscribe to receive email updates on the project.

www.cityofmadison.com/engineering/projects/rutledge-street-reconstruction

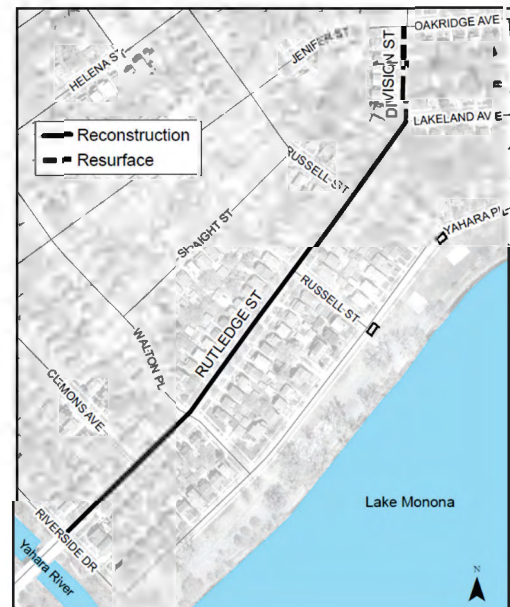

If you have any other questions regarding this project, please contact Nashaly Gutierrez, Project Engineer, at (608) 266-4414, ngutierrez@cityofmadison.com.

Sincerely,



James M. Wolfe, P.E.
City Engineer

JMW:ngv
cc by email:

Marsha Rummel, District 6 Alder
Janet Schmidt, City Engineering
Thomas Mohr, Traffic Engineering
Adam Wiederhoeft, Water Utility
Hannah Mohelnitzky, City Engineering
Tim Sobota, Madison Metro Transit
Jennifer Hannah, Police Department
Cedric D Hodo cdhodo@madison.k12.wi.us
Jenni Lawler jenni@badgerbus.com
John Meier johnm@badgerbus.com

Andrew Zweg, City Engineering
Kyle Frank, City Engineering
Alexandra Heinritz, Traffic Engineering
Lorissa Banuelos, Common Council
Brad Hofmann, City Forestry
Bill Sullivan, Fire Department
Amanda J Nagel ajnagel@madison.k12.wi.us
Dana S Scheel dsscheel@madison.k12.wi.us
John Bain jdbain@madison.k.12.wi.us
Kenneth R Thomas krthomas1@madison.k12.wi.us

Mark Moder, City Engineering
Yang Tao, Traffic Engineering
Nathan Mendez, Water Utility
Charles Romines, Streets Division
Aaron Leair, City Forestry
Dane County 911
